



Regional Class Research Vessel (RCRV)

Status of Construction



National Science Board
November 19, 2019
Brian Midson, RCRV Program Officer



Project Overview

Three Regional Class Research Vessels (RCRVs) are under construction at Gulf Island Shipyards in Houma, LA





Financial Status

Total Project Cost	\$354 million
Contingency	\$56 million
Completion	19%
Progress Cost	99% of expected
Schedule Performance	92% of expected
Confidence	>90%





Schedule Summary





Module 21, Bulbous Bow






Module 22, Shell Plate installation





Shipyard Webcam

<http://webcam.oregonstate.edu/rcrv3>

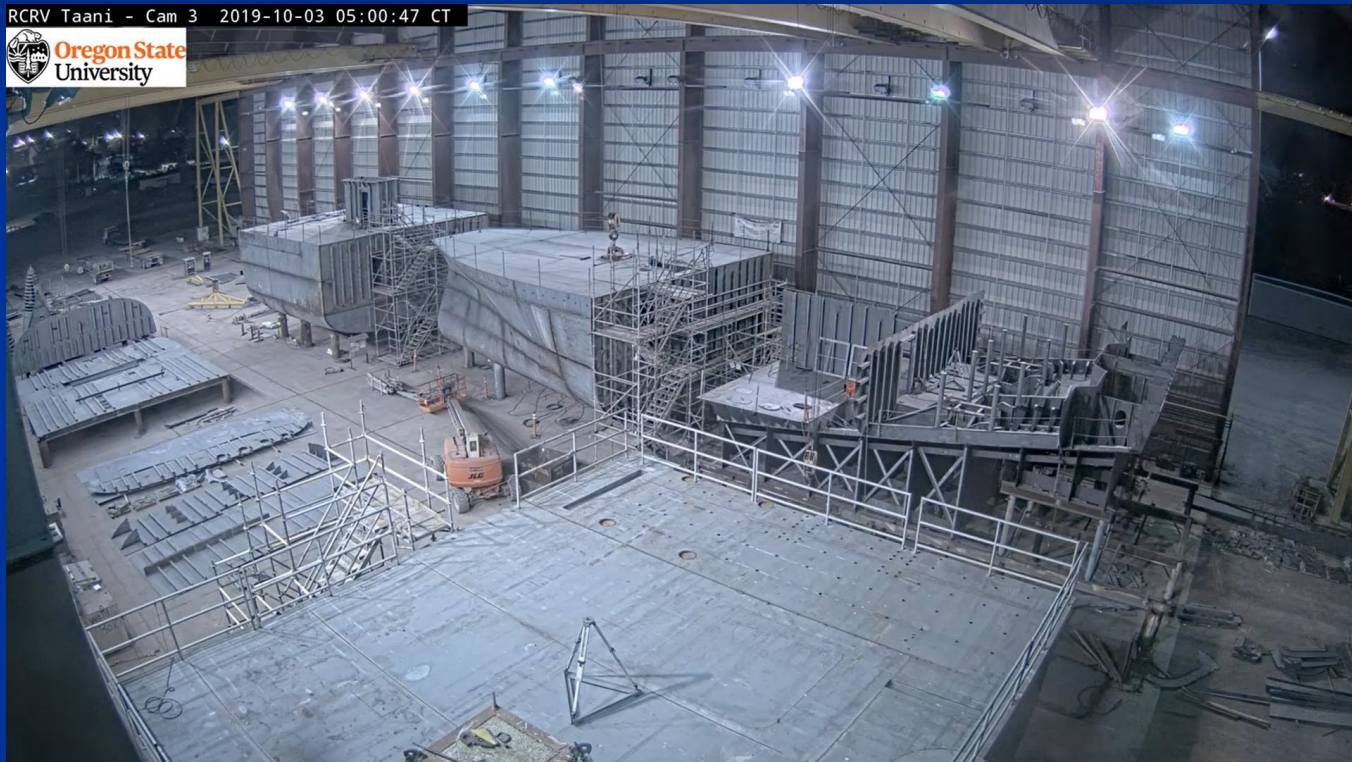

University National Oceanographic Laboratory System
<https://www.unols.org>



Thank you

Questions?
